


# Drip Edge

ANSI/SPRI ES-1 CERTIFIED: .040" Aluminum = 410 psf, 24GA Steel = 390 psf

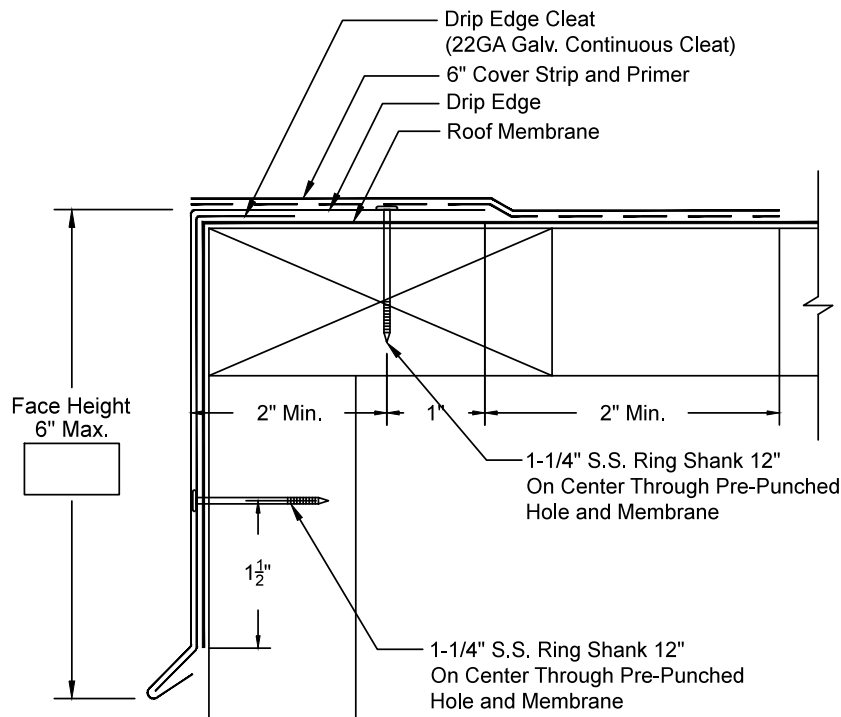

- Continuous Cleat and fasteners provided.
- Concealed Splice Plates provided.
- Splice Plate Sealant available for extra charge.

## PRINT APPROVAL:

Architect and/or Contractor shall verify all dimensions, sizes, and quantities, All products to be installed in strict accordance with Drexel's printed instructions.

Approved By: \_\_\_\_\_

Date: \_\_\_\_\_

## QUANTITIES:

Lineal Feet (10'-0" Lengths\*): \_\_\_\_\_

Outside Miters\*\*: \_\_\_\_\_ ☐ Optional Welded (Surcharge Applies)

Inside Miters\*\*: \_\_\_\_\_ ☐ Optional Welded (Surcharge Applies)

Right End Caps\*\*: \_\_\_\_\_ ☐ Optional Welded (Surcharge Applies)

Left End Caps\*\*: \_\_\_\_\_ ☐ Optional Welded (Surcharge Applies)

Splice Plate Tape Sealant: ☐ Optional Sealant (Surcharge Applies)

\* Optional lengths available up to 20'-0"

\*\* Standard riveted

PROJECT: \_\_\_\_\_

ARCHITECT: \_\_\_\_\_

ROOFING CONTRACTOR: \_\_\_\_\_

REPRESENTATIVE: \_\_\_\_\_

## MATERIAL:

☐ 24GA ☐ .040" AL

☐ Other: \_\_\_\_\_

Finish: \_\_\_\_\_

Color: \_\_\_\_\_

Effective Date: 5-1-13

Drawn By: J.S.

Approved By: B.P.



Toll Free 888-265-4330  
Fax 731-265-4309  
342 Bellvue St Jackson, TN 38301  
www.reelfootmetal.com
